

MARKET SQUARE, DOVER


Newsletter 5 – Refurbishment Updates

April 2022



The paving previously lifted from Cannon Street has been salvaged, checked for damage, cleaned and re-laid.

FM Conway are passionate about reducing waste and reusing materials where possible, materials not able to be reused are recycled and used on sites across the country.

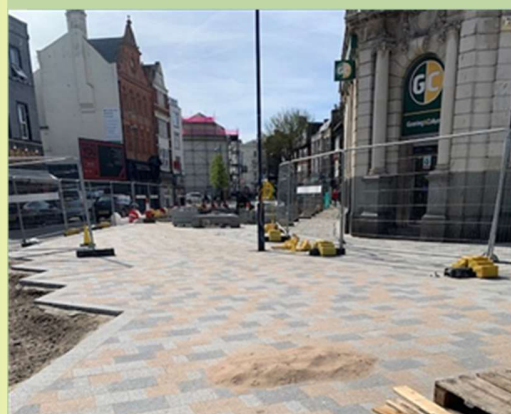


Paving laid along King Street. Work will begin on the west side of the road in the coming weeks.

As part of the social value aspect of the Market Square renovation FM Conway will be starting work on 19th April to improve the entrance to Pencester Gardens.



The consultation on the proposed Traffic Regulation Order on Castle Street will be open for representations from the 15th April 2022 until 9 May 2022. Any representations on the proposed order can be made at www.kent.gov.uk/highwaysconsultations

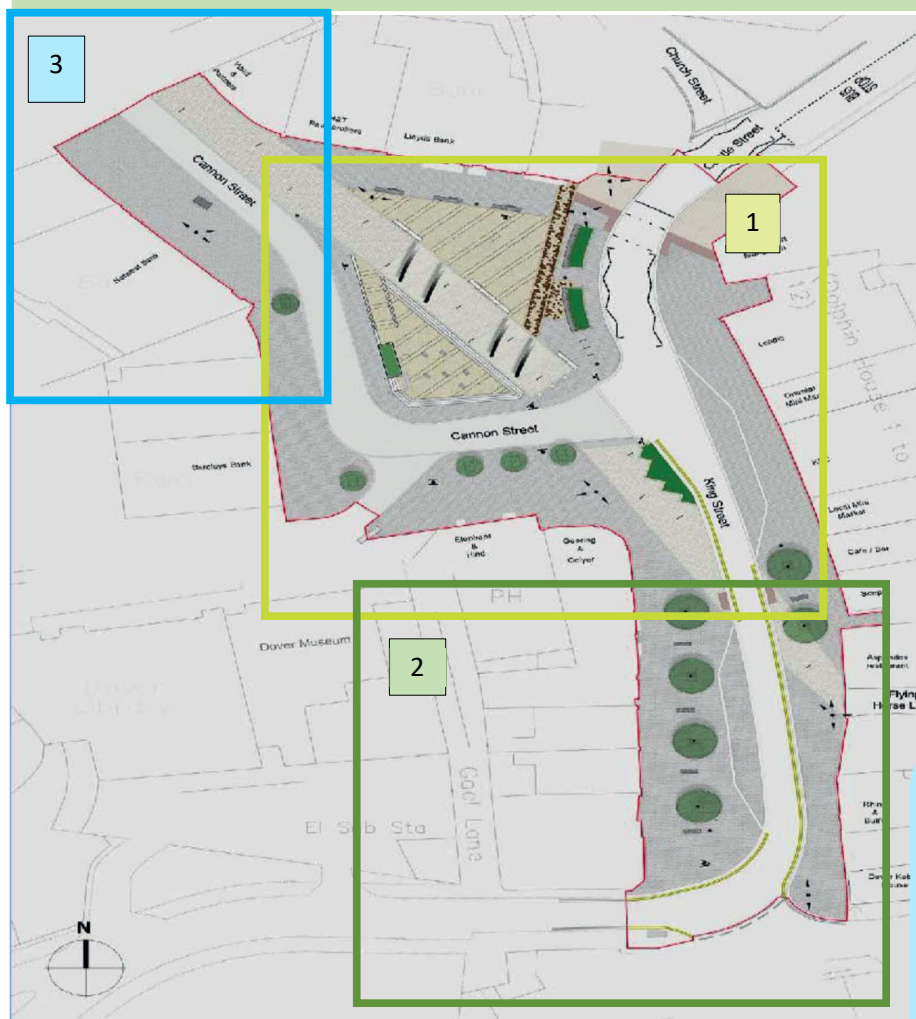

Phase 1 - Market Square Public Realm & Fog Misting feature - 28 weeks

This extends over the full construction period and includes all works within the square. Our colleagues at Affinity Water have carried out works to upgrade the existing water main, this work will ensure the infrastructure is robust enough to accommodate the installation of the bespoke water feature. Construction of the foundations for the steelwork spirals, the new plant room and for the precast concrete units which surround the raised platform, have also started.

Phase 3 – West Side Cannon Street Pedestrian Area - 7 Weeks

The pedestrian area on the west side of Cannon Street will start following completion of the Phase 2 works. The scope and sequence of work is similar to Phase 2 except there are no significant utility works or tree installations required.

Phase 2 – West Side King Street Pedestrian Area & Tree Planting - 10 Weeks

The new bus facility in Castle and Church Street to provide greater flexibility for the bus and coach operators is now in place and operational. Clearance activities including the demolition of raised planters, removal of pedestrian railing and enabling works have been completed. Four new trees are to be planted within this area requiring significant excavation, the root cells and root directors are now in place. Finishing works including installation of lighting, signage and street furniture. Additional soft landscaping and planting of the trees will follow on later in the scheduled works.

FM Conway

Vikki Costello

Mobile: 07501 745 430

Vikki.costello@fmconway.co.uk

www.fmconway.co.uk

Dover District Council

InvestmentAndProjects@dover.gov.uk
