

# MARKET SQUARE, DOVER

Newsletter 7 – Refurbishment Updates


June 2022



The arches for the unique misting feature arrived on 23<sup>rd</sup> June.


Left – The first of the arches being lifted into place

Right – The second arch being placed in the square

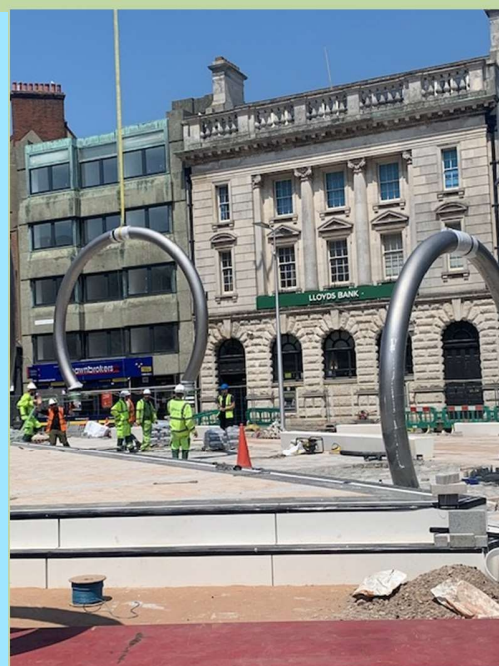

All four arches now have pride of place in the Market Square.

The project is progressing well and with phases nearing completion it is easier to visualise the improved public space. We would like to thank the residents and businesses for your support and patience.

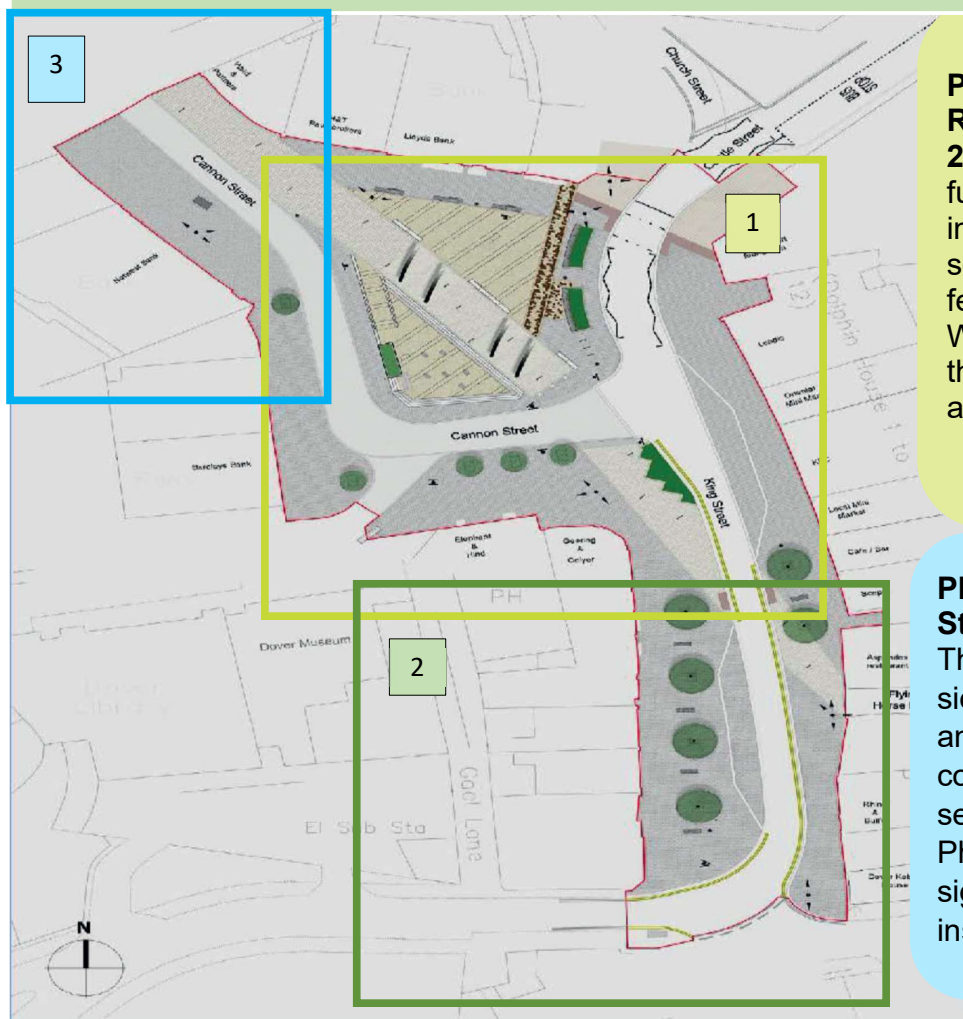

**Phase 1 - Market Square Public Realm & Fog Misting feature - 28 weeks** This extends over the full construction period and includes all works within the square. The bespoke water feature has now been installed. Work is continuing to complete the remaining paving in this area and around the water feature.

**Phase 3 – West Side Cannon Street Pedestrian Area - 7 Weeks** The pedestrian area on the west side of Cannon Street has begun and will continue over the next couple of weeks. The scope and sequence of work is similar to Phase 2 except there are no significant utility works or tree installations required.

**Phase 2 – West Side King Street Pedestrian Area & Tree Planting - 10 Weeks.** The new coach bays in Church Street are now operational. Clearance activities including the demolition of raised planters, removal of pedestrian railing and enabling works have also been completed. Four new trees are to be planted within this area and the root cells and root directors are in place and paving is ongoing. Finishing works including installation of lighting, signage, street furniture, additional soft landscaping and planting of the trees will follow on later in the scheduled works.

## FM Conway

Vikki Costello

Mobile: 07501 745 430

[Vikki.costello@fmconway.co.uk](mailto:Vikki.costello@fmconway.co.uk)

[www.fmconway.co.uk](http://www.fmconway.co.uk)

## Dover District Council

[InvestmentAndProjects@dover.gov.uk](mailto:InvestmentAndProjects@dover.gov.uk)
