

# MARKET SQUARE, DOVER


Newsletter 8 – Refurbishment Updates

August 2022

The Market Square project is coming to a close. There will be a public opening event on the 20th of August 2022 with family activities, music, dance, acrobatic circus and an artisan craft market.




The arches which form the misting feature within the market square have been up and running.

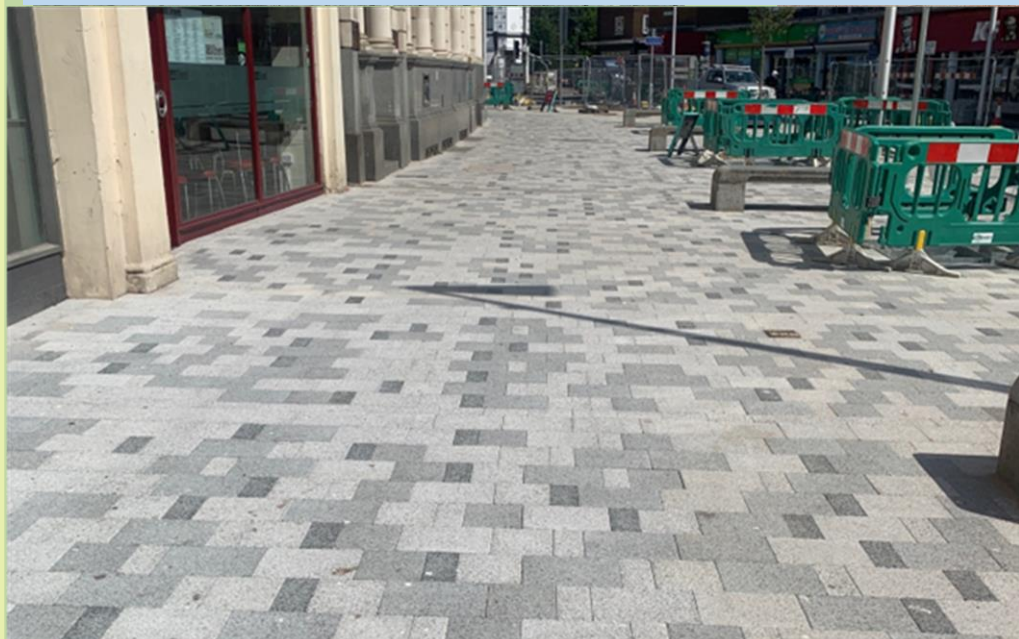

A decision has been made that the planting of the trees on King Street will be delayed until October 2022, this is in order to plant at the correct time of the year to ensure the longevity of the trees.

In the meantime, the tree pits will be filled with temporary asphalt to prevent trip hazards and allow fencing to be removed.

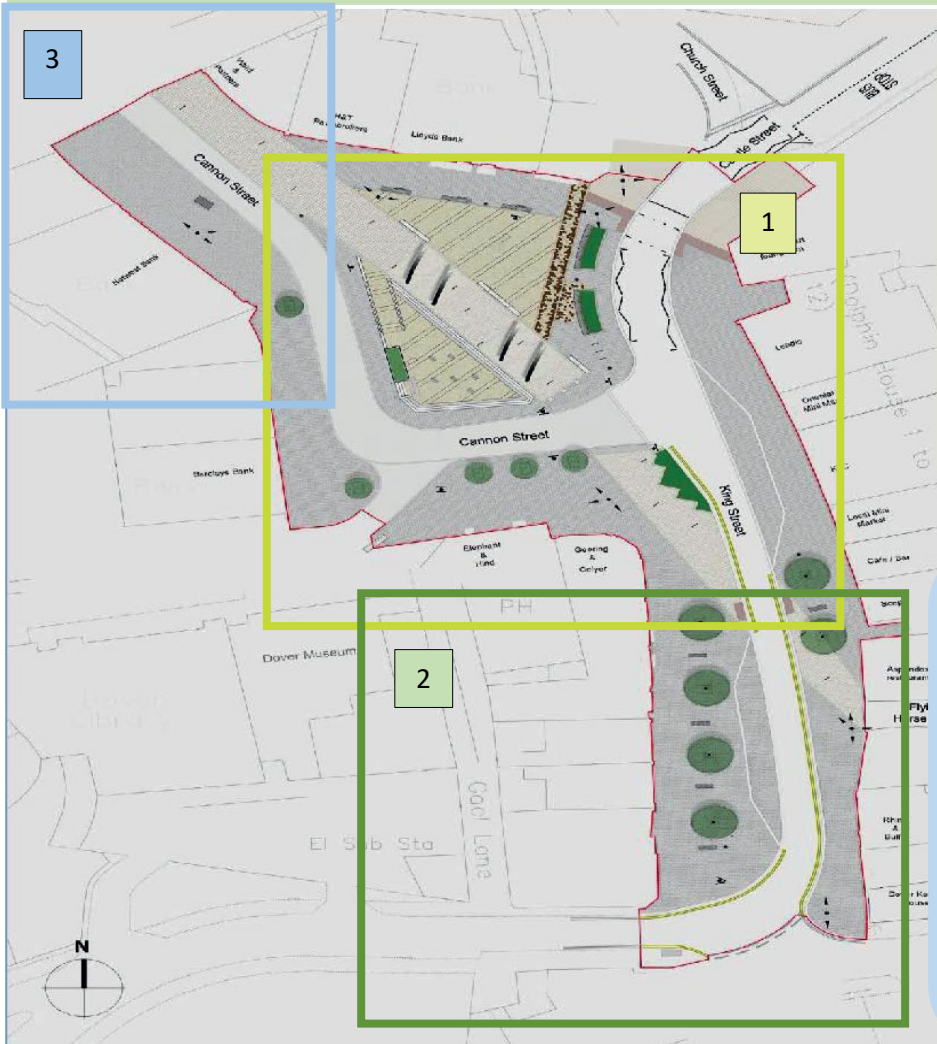

**Phase 1 - Market Square Public Realm & Fog Misting feature - 28 weeks** This extends over the full construction period and includes all works within the square. The bespoke water feature has now been installed and tested. Work is continuing to complete the remaining paving in this area and around the water feature.

**Phase 3 – West Side Cannon Street Pedestrian Area - 7 Weeks** The pedestrian area on the west side of Cannon Street has been completed.

**Phase 2 – West Side King Street Pedestrian Area & Tree Planting - 10 Weeks.** Six new trees are to be planted within this area in October 2022. Paving is now complete.

A small number of FM Conway workers will remain on site for a few days following completion of the project in order to rectify small imperfections and ensure the highest quality finish on the project.

**FM Conway**  
 Vikki Costello  
 Mobile: 07501 745 430  
[Vikki.costello@fmconway.co.uk](mailto:Vikki.costello@fmconway.co.uk)  
[www.fmconway.co.uk](http://www.fmconway.co.uk)

**Dover District Council**  
[InvestmentAndProjects@dover.gov.uk](mailto:InvestmentAndProjects@dover.gov.uk)
